
Costs and Benefits of Commissioning **New and Existing Commercial Buildings**



Evan Mills, Norman Bourassa, and Mary Ann Piette Lawrence Berkeley National Laboratory



Hannah Friedman and Tudi Haasl P E C I Portland Energy Conservation, Inc.



David Claridge and Tehesia Powell Texas A&M University - Energy Systems Lab

Sponsors: U.S. Department of Energy (this study); CEC-PIER (related work)

Commissioning is Quality Assurance

- Articulating/verifying design intent
- Construction observation; warranty enforcement
- Controlling first cost
- Training operators
- Optimizing performance (comfort, reliability, safety, energy)
- Enhancing safety and risk management

History

- Born in ship-building industry
- Originally applied in buildings in early 1980s to ensure performance of energy efficiency measures
- Later realized that "ordinary" buildings could achieve energy savings by correcting deficiencies
- Many initiatives/drivers:
 - R&D (e.g. California PIER)
 - Utility programs
 - LEED (required step)
 - California Green Buildings Executive Order and Green Buildings Action Plan
 - California Commissioning Collaborative


Perhaps the single most important outstanding question is:

"Is it Cost-Effective?"

Is There a Need?


- Building problems (a.k.a. "deficiencies") are pervasive
 - Design flaws; Construction defects; Malfunctioning equipment; Deferred maintenance
 - Don't shoot the messenger: problems a combined result of fragmentation/specialization of trades, "value" engineering, increasingly complex building design and operation requirements, lack of clear design-intent documentation and performance targets, etc.
- Not attending to problems can cause:
 - Discomfort --> Eroded productivity, absenteeism
 - Indoor air quality problems
 - Premature equipment failure
 - Litigation
 - Excessive energy and construction costs
- Many problems can be cost-effectively remedied

Broken Dampers

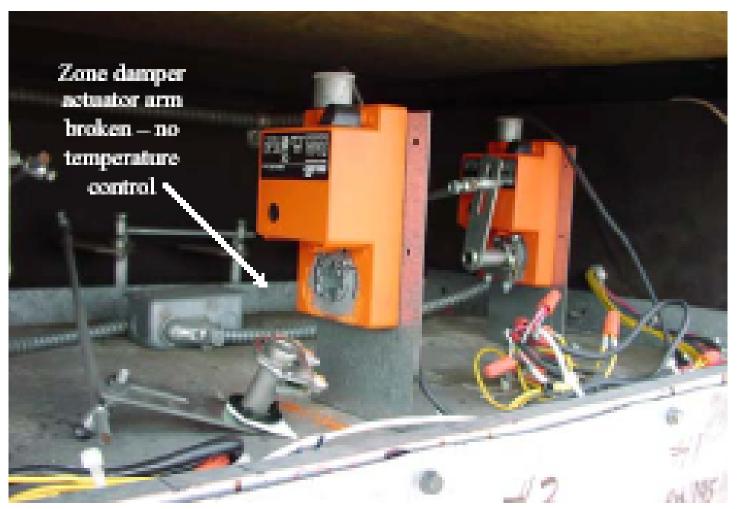


Broken actuator arm on damper of multizone unit, elementary school

Fouled filters

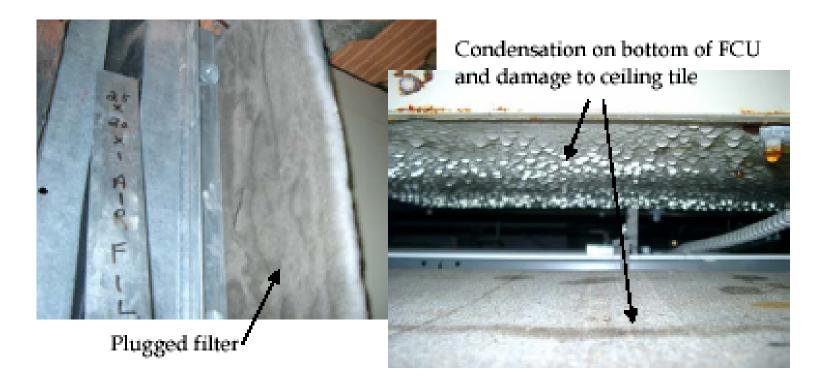

Condensation damage from DX fan coil unit due to plugged filter and low air flow. Large high school.

Faulty controls

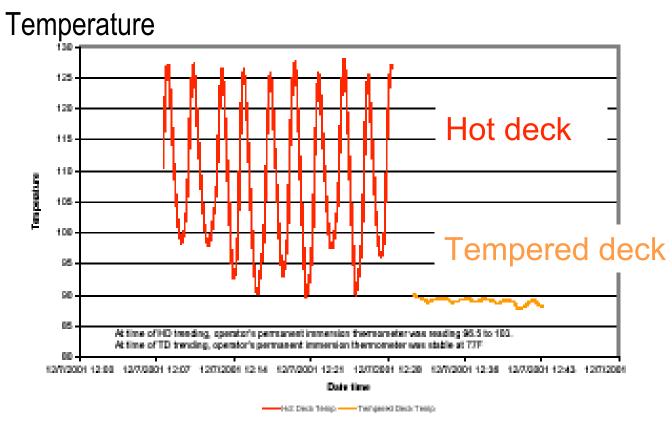

Hunting of hot deck temperatures with pneumatic control due to sensor thermal mass, steam valve sizing, and controller proportional band. Older high-rise office building.

Poor Coordination Among Trades



Inadequate cooling and excessive fan power consumption due to poor fit between light troffer diffusers and duct boot provided by a different supplier, allowing up to 25% of flow at diffuser to bypass directly into ceiling plenum. Highrise office tower.


Envelope: air leakage and moisture management



Damage to brick facade of pool building due to lack of specification for (a) sealing of air leakage paths in exterior envelope and (b) balancing to assure negative pressurization of pool area. Large newer middle school.

Design-operation mismatch

Actual/Required air flow

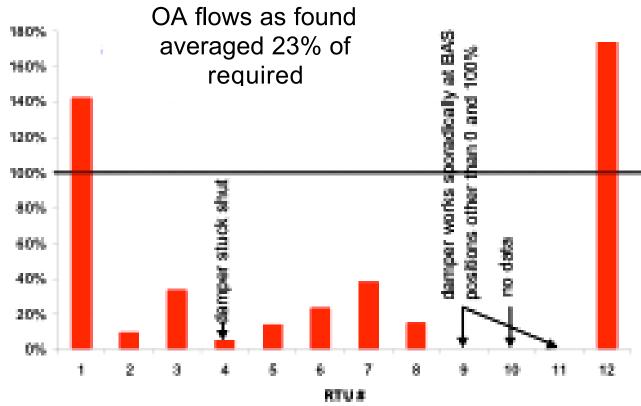


Outside air flows as a percent of required air flow for current occupancy and ventilation standards. Twelve rooftop units at an elementary school.


Energy consequences


DOE High-Performance Buildings Case Studies: Goals vs. Actual

Energy Cost Savings

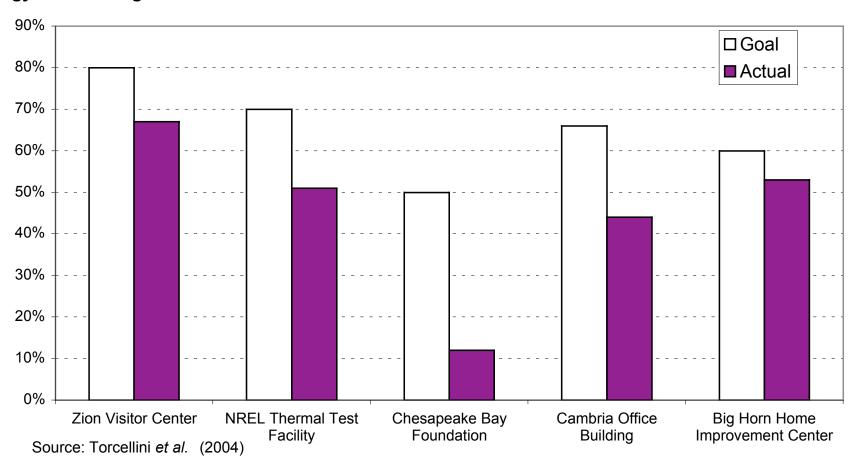

Case Study: Kleberg Building

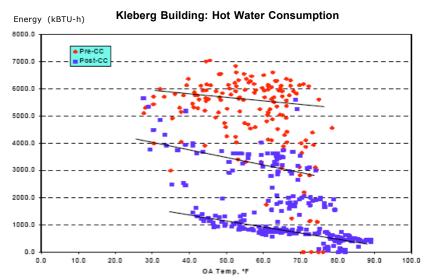

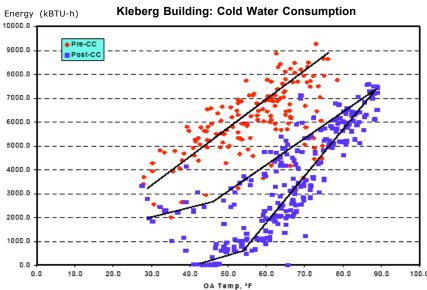

INITIAL CONDITION - upper [red] clouds

Continuous preheat - 105F (intentional)

PHASE 1 MEASURES - middle [blue]

Preheat off

PHASE 2 MEASURES - lower [blue]

- Preheat to 40F
- Optimize cold deck temps
- Reactivate economizer mode
- Static pressure optimization
- Night-time setback
- Replaced or repaired VFD boxes
- Restarted chilled water VFD
- CHW pump control staging
- · Building stack pressure reduced
- Fume hood exhaust pressure reduced

IMPACTS

- Chilled water: 64% reduction
- Hot water: 84% reduction
- \$314,000 annual energy cost savings

Main Characteristics of Our Study

- Meta-Analysis (some primary information)
- Focus on energy aspects, but also non-energy impacts
- Separate treatment of existing and newly constructed buildings
- Standardized analysis (definitions, normalized energy prices, inflation) -- has significant effect on results
- Extensive statistical and correlation analyses

Methodology

- Establish metrics
- Develop standardized language for describing Cx scope
- Develop standardized framework for characterizing deficiencies and measures ("Measures Matrix")
- Design data instrument to collect required information
- Collect data: from the literature and Cx providers
- Review data quality
- Perform normalizations
 - Standardized energy prices
 - Construction costs corrected for inflation (\$2003)
 - Commissioning costs corrected for inflation (\$2003)
- Analysis and inter-comparisons (including IPMVP bins)
- Analyze subgroups (new/existing; building type)
- Identify correlations (or lack thereof)
- Identify data gaps

Information Compiled (top level, ~ 200 fields)

- Commissioning provider
- Building type, size, location
- Costs of commissioning (all parties)
- Normalization data (prices, years, weather)
- Observed benefits
 - Energy (IPMVP classifications, or estimates)
 - non-energy
- Commissioning Scope
- Measures Matrix
 - Types of problems ("deficiencies") discovered
 - Types of interventions ("measures") implemented

Resulting Sample Characteristics

- 224 buildings (175 projects), of which 150 are existing buildings and 74 are new construction
 - 18+ commissioning providers
 - Largest sample yet compiled
- Diversity of building types (heavy on public buildings)
- 30.4 million square feet across 21 U.S. states
 - Existing buildings: median 151,000 ft²
 - New construction: median 69,500 ft²
- \$17 million investment
- Projects span two decades, but most done in the 1990s



Top-level Findings


- Existing Buildings
 - Cost: \$0.27/ft² Median NEBs: \$0.18/ft²
 - Deficiencies: 11 per building
 - Energy Savings: 15%
 - Payback: 8.5 months
- New Construction
 - Cost: \$1.00/ft² Median NEBs: \$1.24/ft²
 - Deficiencies: 28 per building
 - Payback: 4.8 years
- Cost-effective over range of energy intensities, bldg types, sizes, locations
- Most successful: energy-intensive buildings
- Cost-effective outcomes harder in small buildings
- Energy savings rise with more thorough commissioning

Commissioning Scope: Existing Buildings


- Develop or update design intent documentation
- Plan
- Utility analysis, benchmarking
- Trend analysis
- Building modeling
- Findings
- Estimate benefits from interventions
- Update system documentation (e.g. control sequences)
- O&M improvements
- Capital improvements (grey zone)
- Monitor fixes
- Measure impacts
- Systems manual/recommissioning manual
- Report

Scope

Share of projects including given activity

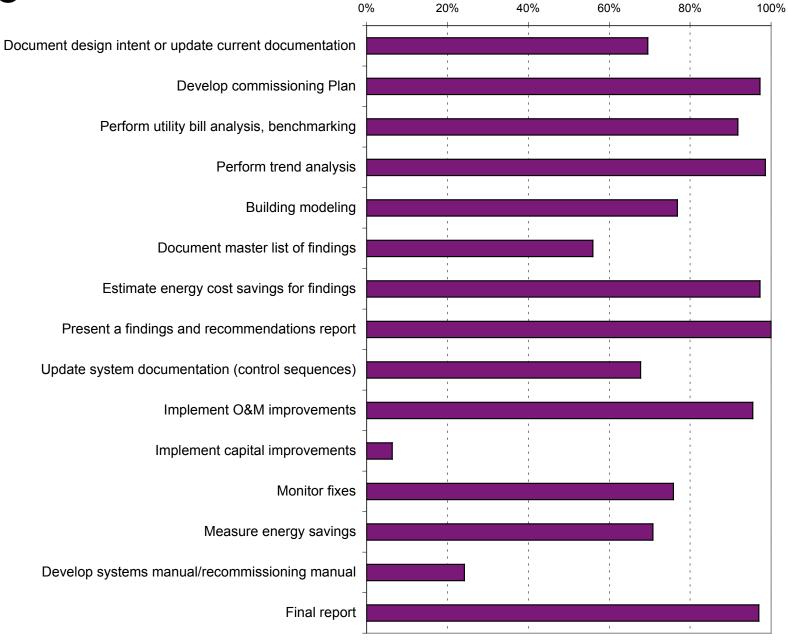


Savings Scale with Commissioning Scope

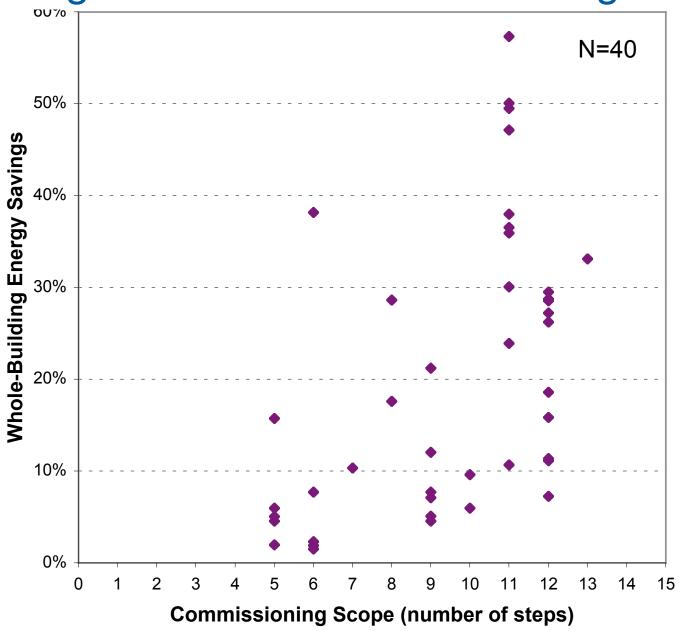


Commissioning Scope: New Construction

- Develop design intent documents
- Specifications
- Plan
- Design review
- Sequences of operation (if not already available)
- Review submittals
- Construction observation
- Verification checks
- Functional testing
- Issue resolution
- Training
- Review O&M manuals
- Systems manual/recommissioning manual
- Trend analysis; evaluate energy savings
- Report

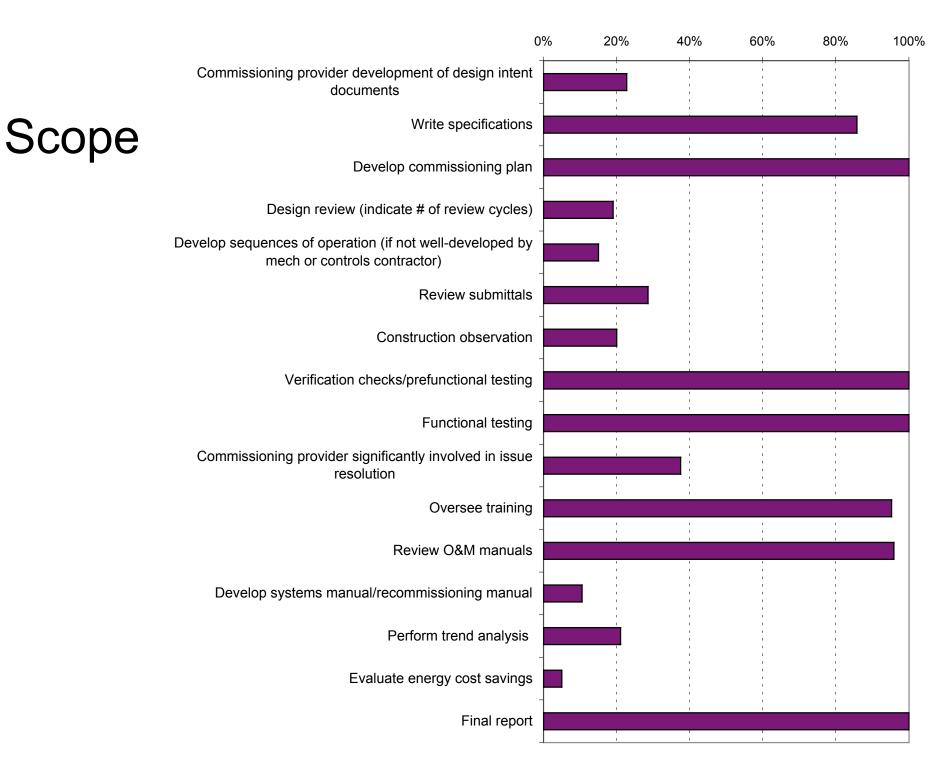


Drivers: Existing Buildings

Reasons for Existing Buildings Commissioning (N=85)

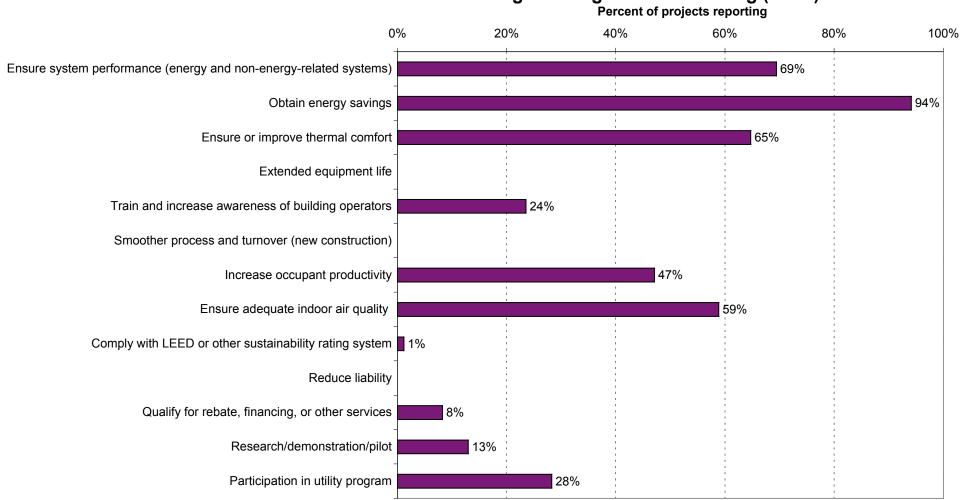

Drivers: New Construction


Reasons for New-Construction Commissioning (N=30) Percent of projects reporting

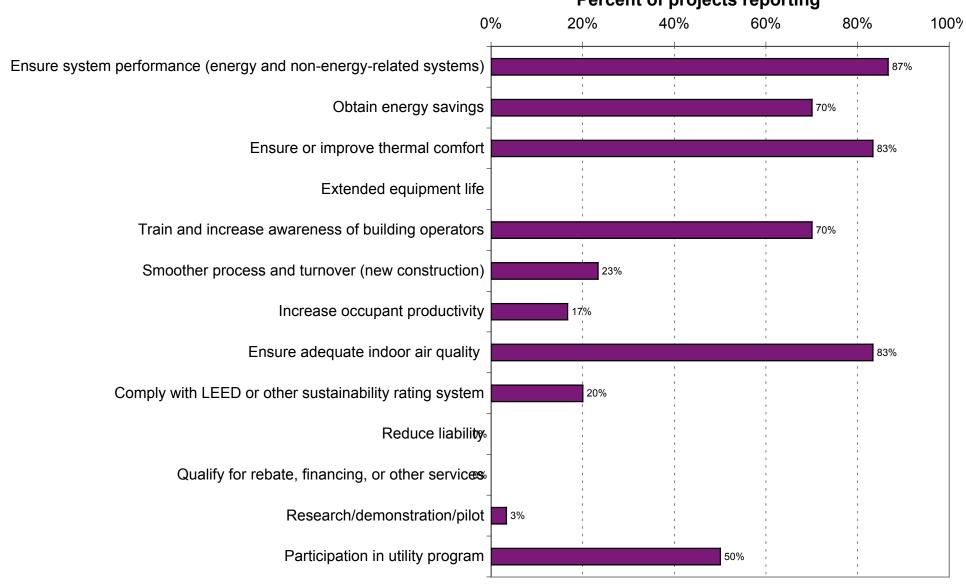

Types of Deficiencies Discovered



Number of Deficiencies Identified by Building System (New Construction, N = 3,305)

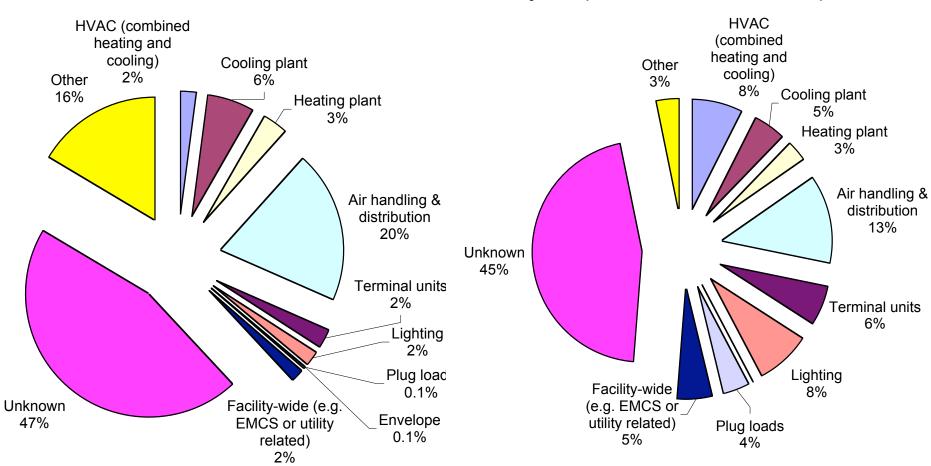


Results from Measures Matrices: Existing buildings (69 projects) [yellow highlights indicate most common measures, deficiencies, and combinations].


		Design, Installation, Retrofit, Replacement				Operations & Control									Maintenance					
N (paired) = 702	Design change	Installation modifications	Retrofit/equipment replacement	Other	Implement advanced reset	Start/Stop (environmentally determined)	Scheduling (occupancy determined)	Modify setpoint	Equipment staging	Modify sequence of operations	Loop tuning	Behavior modification/manual changes to operations	Other	Calibration	Mechanical fix	Heat transfer maintenance	Filtration maintenance	Other	Deficiency unmatched to specific measure	
Deficiencies	D1	D2	D3	D4	100	002	003	0C4	005	oce	007	900	000	M1	M2	M3	M4	M5	Defic	Total
HVAC (combined heating and cooling) V	0		8	1	1	1	5		1	5	0	0	2			1	5	2	12	61
Cooling plant C		ı	19	0	26	5	4	10	4	27	3	12	2			1		0	13	155
Heating plant H	4	0		0	15	7	1	4	0	7	1	5	1	4	7	1	0	0	18	80
			5	·				• 1			- 1									00
Air handling & distribution A	15	9	19	3	80	9	21	25	4	24	12	14	6	40	27	3	4	2	40	357
Terminal units T	15 1	9	19 2	·	80 4	9	21 3	25 14	4	24 4	12	14 2	6 1	40 7	27 10	3	4	0		357 61
Terminal units T Lighting L	15 1 3	9 3 1	19 2 17	3 1 1	80 4 1	9 0 2	21 3 4	25 14 0	4 0 0	24 4 0	12 1 0	14 2 5	6 1 0	40 7 2	27 10 1	3 0 0	4 0 0	0	40	357
Terminal units T Lighting L Envelope E	15 1 3 0	9 3 1 0	19 2 17 0	3 1 1 0	80 4 1 0	9 0 2 0	21 3 4 0	25 14 0 0	4 0 0 0	24 4 0 0	12 1 0 0	14 2	6 1 0	40 7 2 0	27 10 1 0	3 0 0	4 0 0 0	0 0 0	40	357 61
Terminal units T Lighting L Envelope E Plug loads P	15 1 3 0	9 3 1 0	19 2 17 0 0	3 1 1 0 0	80 4 1 0 0	9 0 2 0 0	21 3 4 0	25 14 0 0	4 0 0 0 0	24 4 0 0	12 1 0 0	14 2 5 0	6 1 0 0	40 7 2 0	27 10 1 0 0	3 0 0 0	4 0 0 0 0	0 0 0	40 8 1	357 61 38
Terminal units T Lighting L Envelope E Plug loads P Facility-wide (e.g. EMCS or utility related) F	15 1 3 0 0 2	9 3 1 0 0 3	19 2 17 0 0 2	3 1 1 0 0	80 4 1 0 0	9 0 2 0 0	21 3 4 0 0 7	25 14 0 0 0	4 0 0 0 0 0	24 4 0 0 0 1	12 1 0 0 0	14 2 5 0 1 7	6 1 0 0 0 2	40 7 2 0 0 2	27 10 1 0 0 2	3 0 0 0 0	4 0 0 0 0	0 0 0 0	40 8 1 0	357 61 38 0 1 34
Terminal units T Lighting L Envelope E Plug loads P	15 1 3 0 0 2	9 3 1 0 0 3	19 2 17 0 0	3 1 1 0 0	80 4 1 0 0	9 0 2 0 0	21 3 4 0	25 14 0 0 0	4 0 0 0 0	24 4 0 0	12 1 0 0	14 2 5 0	6 1 0 0	40 7 2 0 0	27 10 1 0 0 2	3 0 0 0 0	4 0 0 0 0 0	0 0 0 0	40 8 1 0	357 61 38 0
Terminal units T Lighting L Envelope E Plug loads P Facility-wide (e.g. EMCS or utility related) F	15 1 3 0 0 2	9 3 1 0 0 3	19 2 17 0 0 2	3 1 1 0 0 0	80 4 1 0 0	9 0 2 0 0	21 3 4 0 0 7	25 14 0 0 0	4 0 0 0 0 0	24 4 0 0 0 1	12 1 0 0 0	14 2 5 0 1 7	6 1 0 0 0 2	40 7 2 0 0 2	27 10 1 0 0 2 3	3 0 0 0 0 1	4 0 0 0 0 0 0	0 0 0 0 0	40 8 1 0 0 3	357 61 38 0 1 34

Cost Allocation

Existing Buildings (N=55)

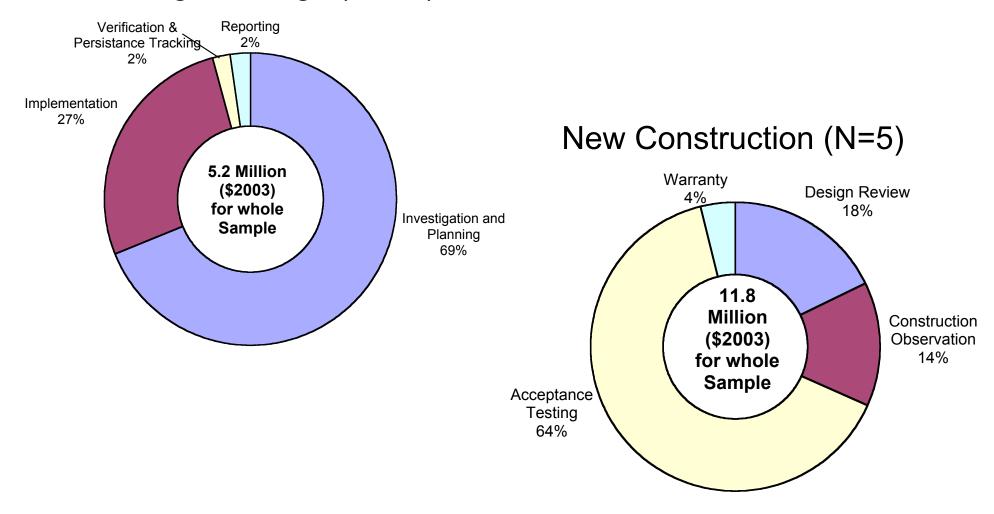


Normalized Costs

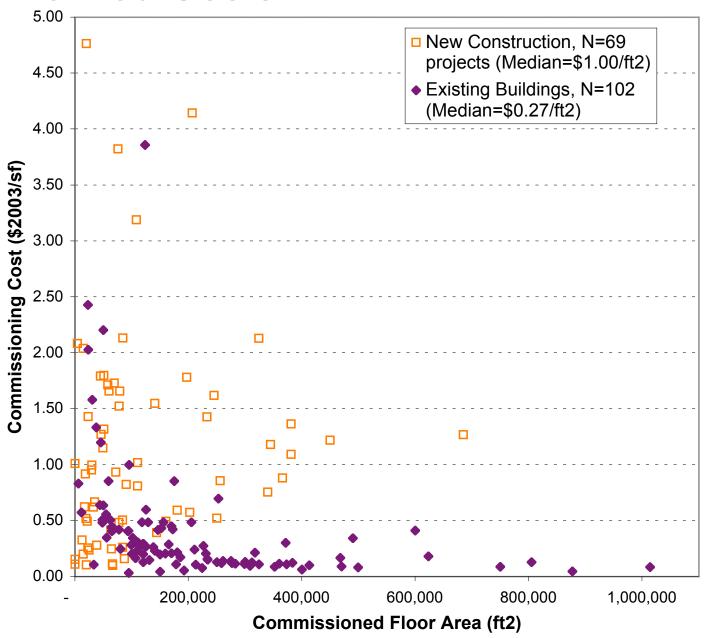


Observed Non-Energy Impacts


Existing Buildings (N=55)

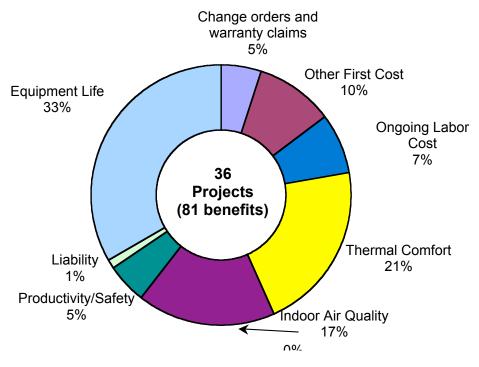


New Construction (N=5)

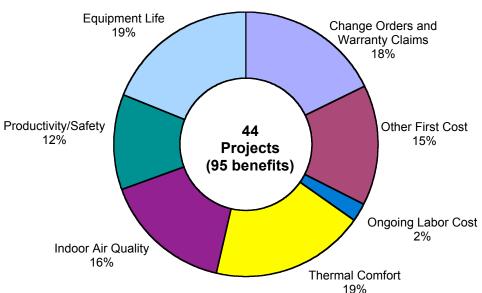

Non-Energy Benefits Often Offset Cost of Commissioning

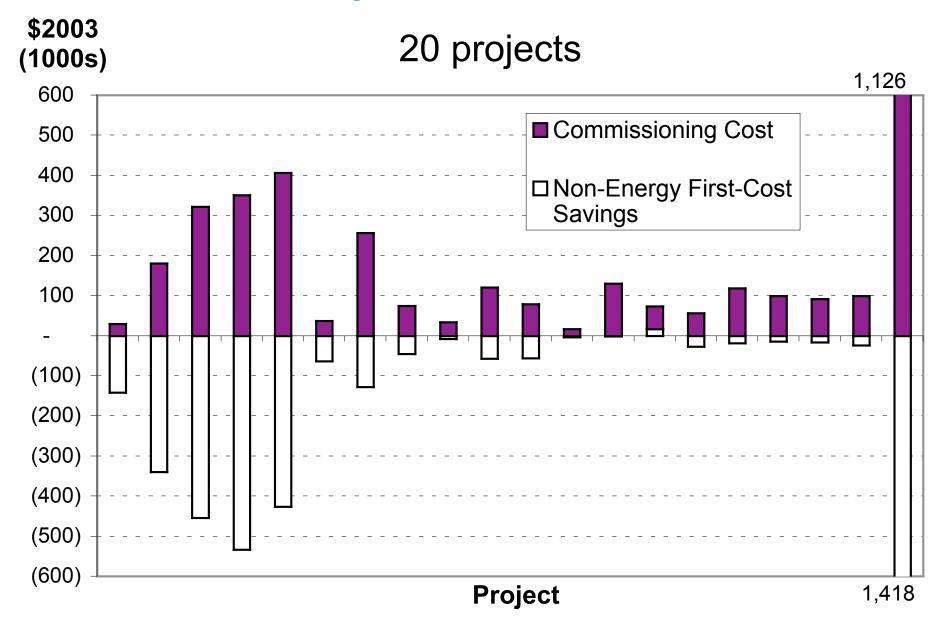


New Construction: Costs range from -1% to 2%+ of total construction cost

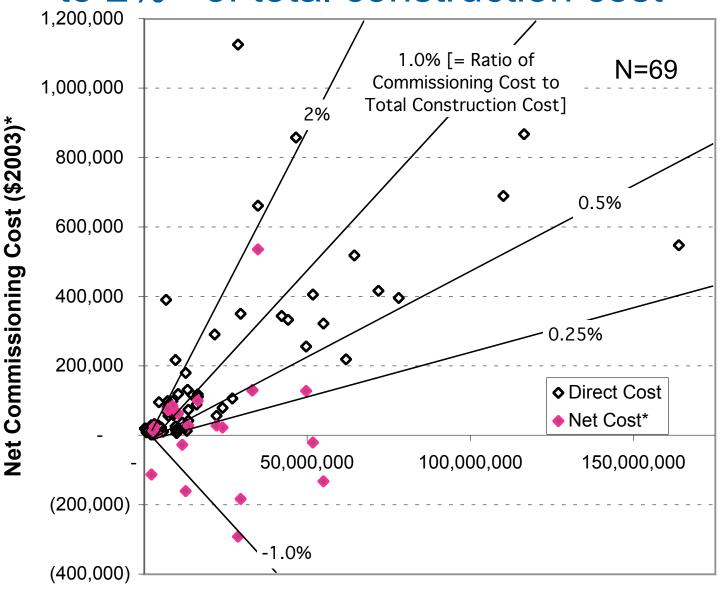


Inclusion of non-energy benefits (e.g. equipment downsizing, reduced callbacks, ... significantly reduces costs


Building Construction Cost (\$2003)

Up to 50% Whole-Building Energy Savings

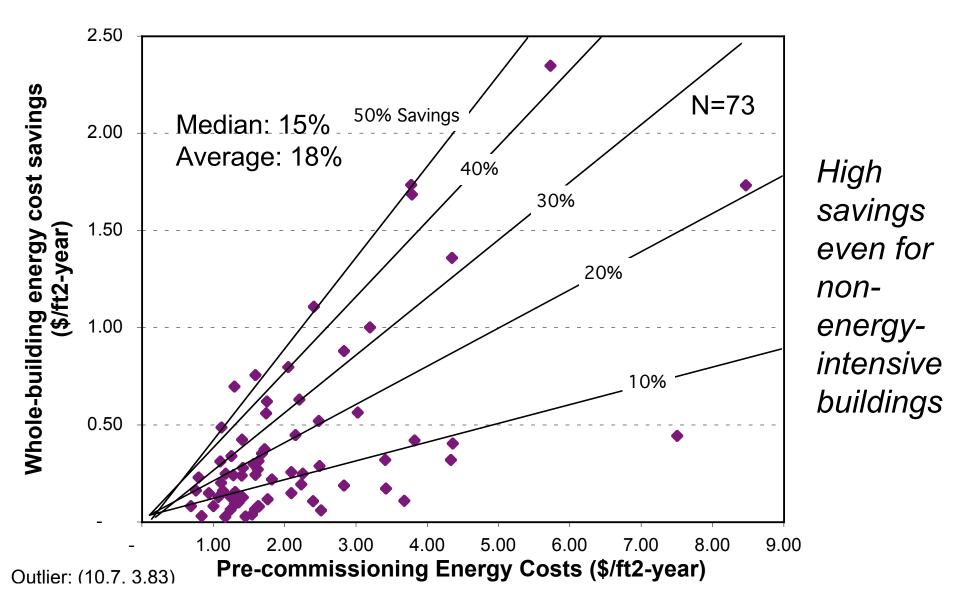


Energy Savings & Payback Times Independent of Pre-Cx Energy Intensities




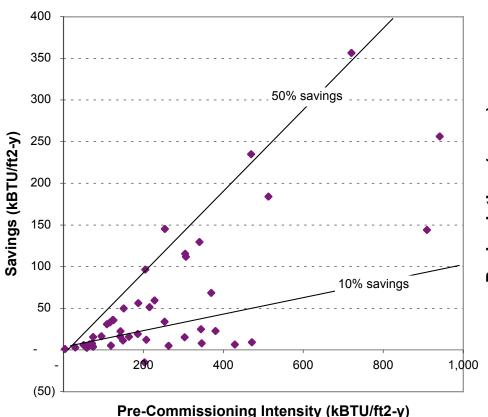


Payback Time vs. Pre-Retro-Commissioning EUI (Existing Buildings)

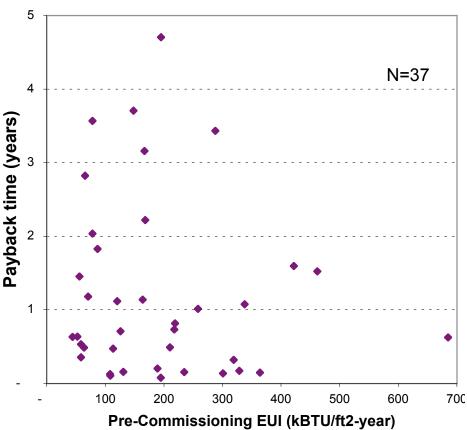


Payback Times: Existing Buildings

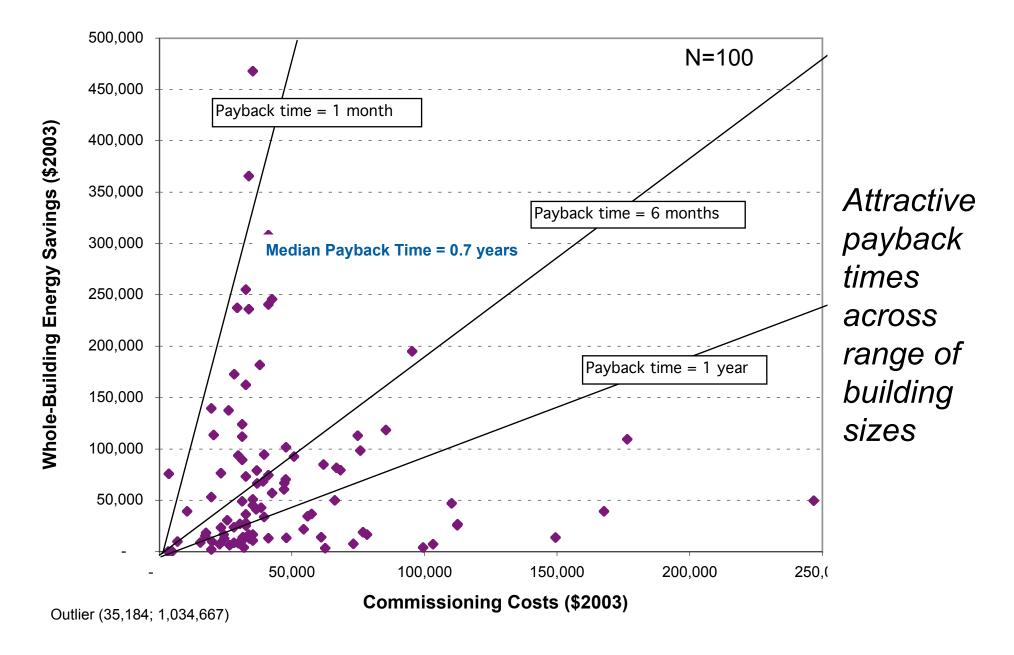

Payback Times: New Construction

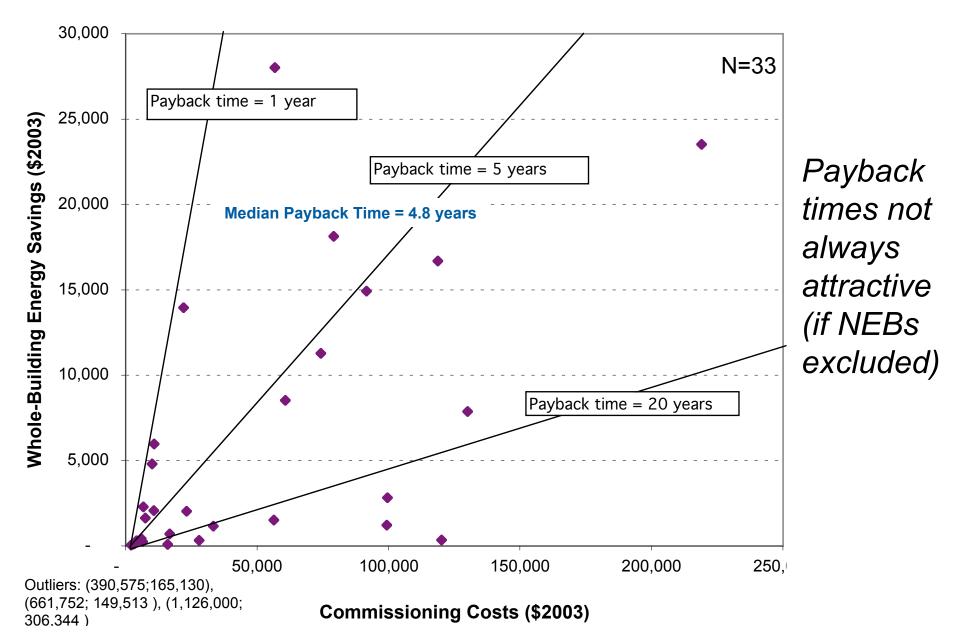


Results Vary by Building Type

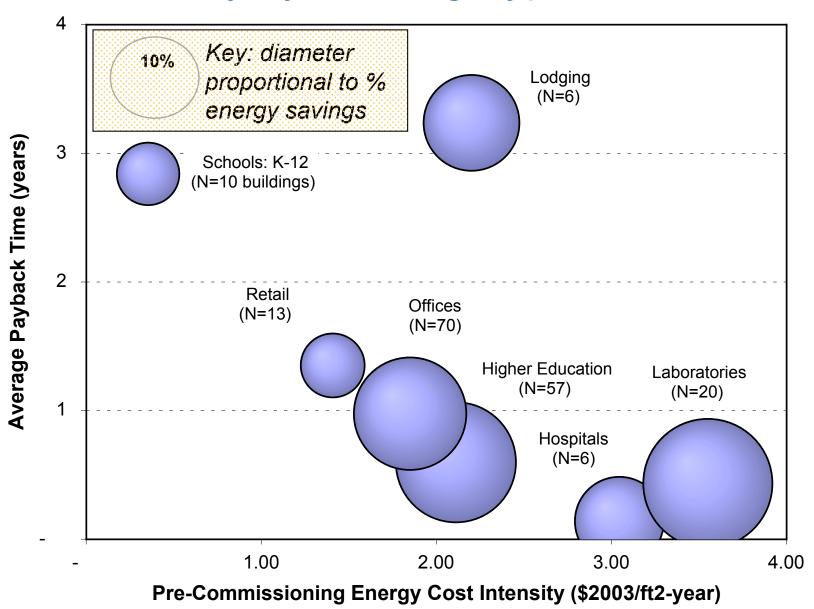

Excluding non-energy impacts

Emergence & Persistence of Energy Savings

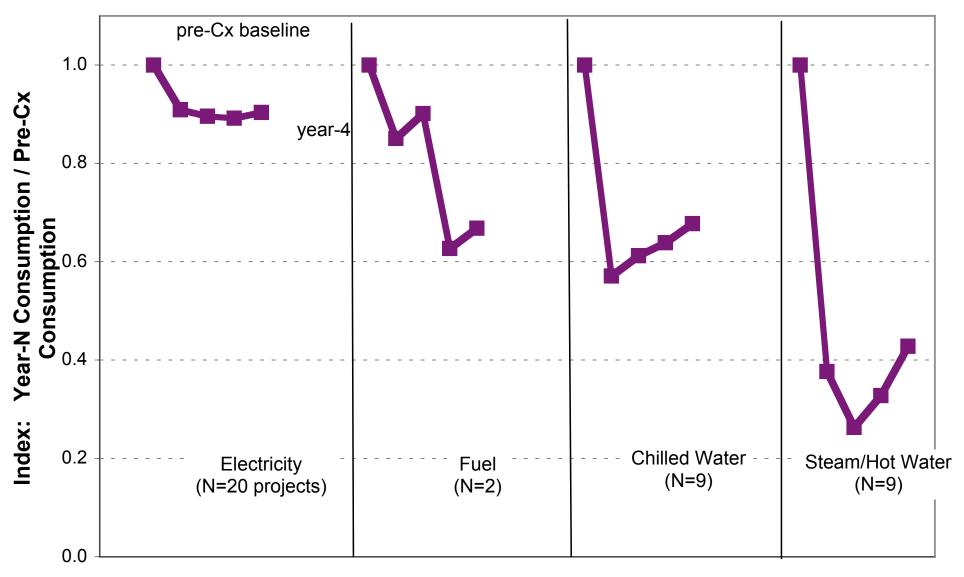

Time following Commissioning (4 years per project)

Existing Buildings vs. New Construction

- Existing buildings
 - larger
 - greater normalized energy savings
 - more cost-effective (excluding NEBs)
- New construction
 - less comprehensive
 - normalized costs higher
 - larger non-energy benefits
 - NEBs are a more important motivation for embarking on commissioning, and can go farther in offsetting the cost of commissioning
 - more deficiencies found

National Potential; National Need

 \$18 billion <u>annual</u> energy savings potential (US-wide) -- plus non-energy benefits

 Without commissioning, many energyefficiency projects, programs, and policies will often fall short of their goals

Recommendations

- No energy management program is complete without commissioning (in-house or outsourced)
- Invest in commissioning (existing buildings and new construction)
- Institutionalize the process
- Track outcomes, refine process

Participate in our Research:
Evan Mills
Lawrence Berkeley National Laboratory
510-486-6784 • emills@lbl.gov

http://eetd.lbl.gov/emills/PUBS/Cx-Costs-Benefits.html
